



NEC[®] Users' Group Annual Seminar 2014

*Dynamic Infrastructure
and project delivery*

28 APRIL | LONDON

NEC in Hong Kong



Ir. TSUI Wai

**Deputy Director of Drainage Services
Drainage Services Department**

The Government of the Hong Kong Special Administrative Region

28 April 2014




渠務署

Drainage Services Department

Agenda



- 
- A high-speed train, likely a Shinkansen, is shown in motion on a track, with a green overlay. The train is white with blue and grey accents, and the background is blurred to indicate speed.
- Use of NEC in Hong Kong
 - Opportunities and Challenges
 - NEC Adaptation in Hong Kong

Background



Procurement of Projects in Hong Kong Government

Stores and Procurement Regulations

■ Works Contracts

- Central Tender Board
- General Conditions of Contract (GCC) (1999)

■ Consultancy Agreements

- Engineering & Associated Consultants Selection Board
- General Conditions of Employment of Engineering and Associated Consultants (GCE) (1997)


Background



General Conditions of Contract (GCC)

- A family for various types of works contract
- Based on ICE Conditions of Contract


General Conditions of Employment of Engineering and Associated Consultants (GCE)



Background



Works Departments in Hong Kong

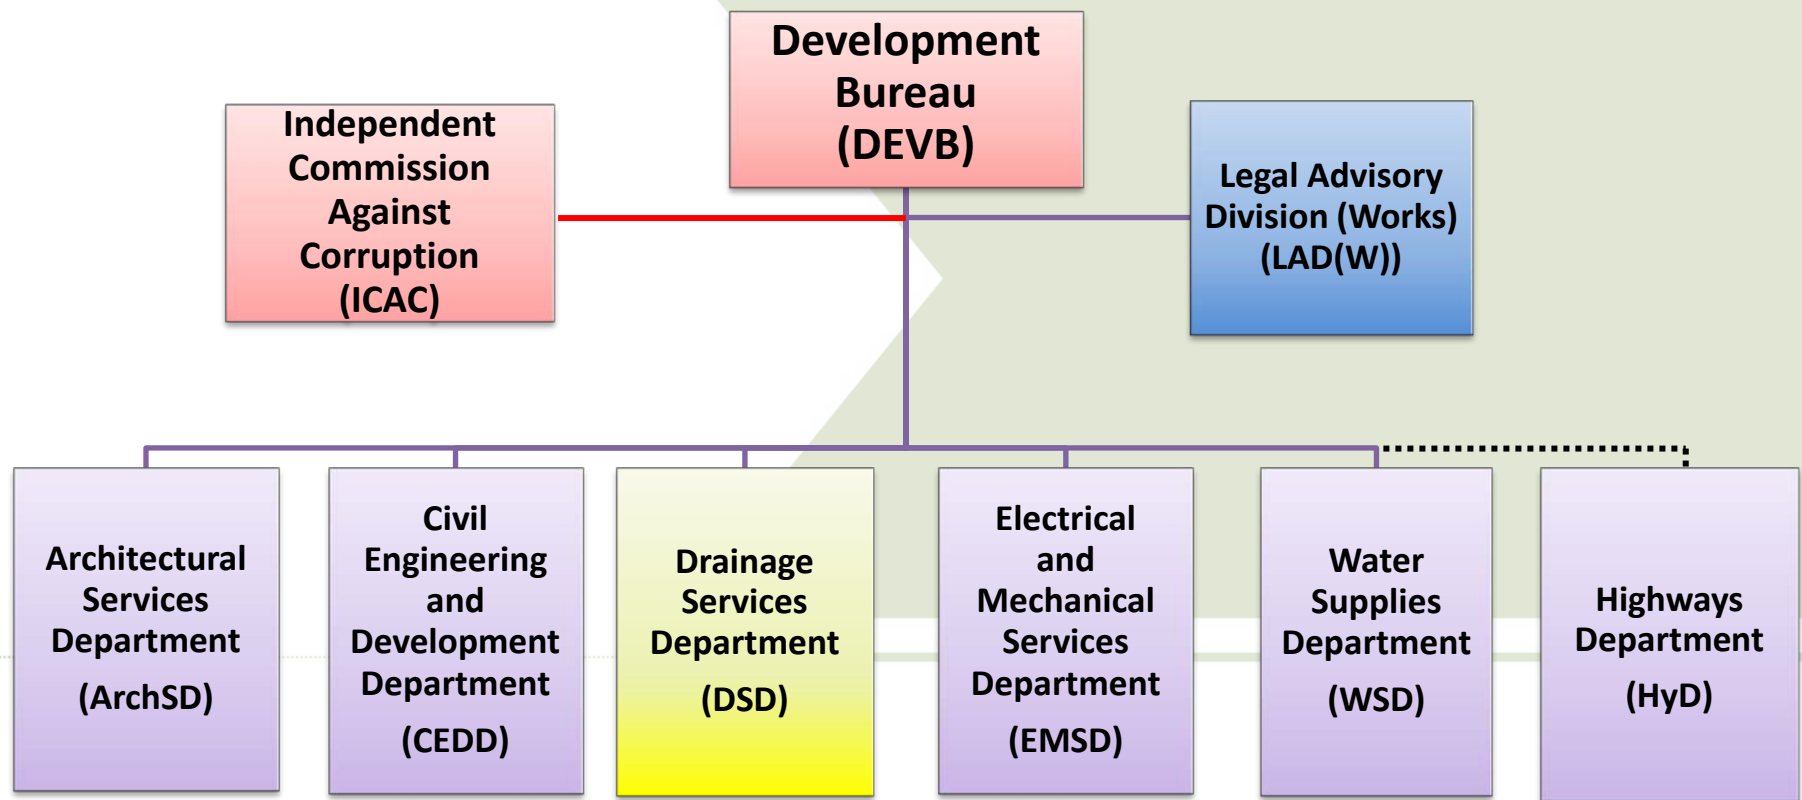


渠務署

Drainage Services Department

Background



- General Conditions of Contract (GCC)
 - Higher risks allocated to Contractor
 - Higher chance of dispute
 - Adversarial

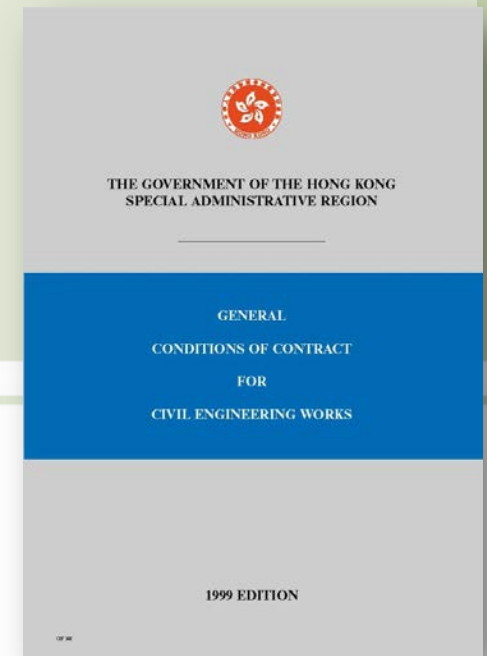

Background



- *Construction Industry Review Committee (CIRC) Report – January 2001*

“Construct for Excellence”

- Partnering
- Integrate partnering to contractual relationship
- Alternative payment methods
e.g. target cost, pain-gain share



Background



■ *From 2001*

- Non-contractual partnering
- But under adversarial contract form

■ *In 2006, Hong Kong Government Decided to Take One Step Further*

- Adopt NEC3 – contractual partnering
- DSD – 1st works department for pilot trial on NEC ECC



1st NEC Contract in DSD and in Hong Kong Government




Planning of 1st NEC Contract in DSD



Engage NEC Advisor
(Oct 2006)



NEC Working Group
(2007)



Work Contract Signing
(Aug 2009)



香港建造商會
Hong Kong Construction Association

Consult Hong Kong
Construction
Association, Organize
NEC Workshops and
Dummy Tender Exercise
(2009)



Seek Advice on
legal and
administrative
measures
(2007-2009)



Seek Advice on
anti-corruption
from ICAC
(2007-2009)




渠務署

Drainage Services Department

1st NEC Contract in DSD and in Hong Kong Government



Planning of 1st NEC Contract in DSD

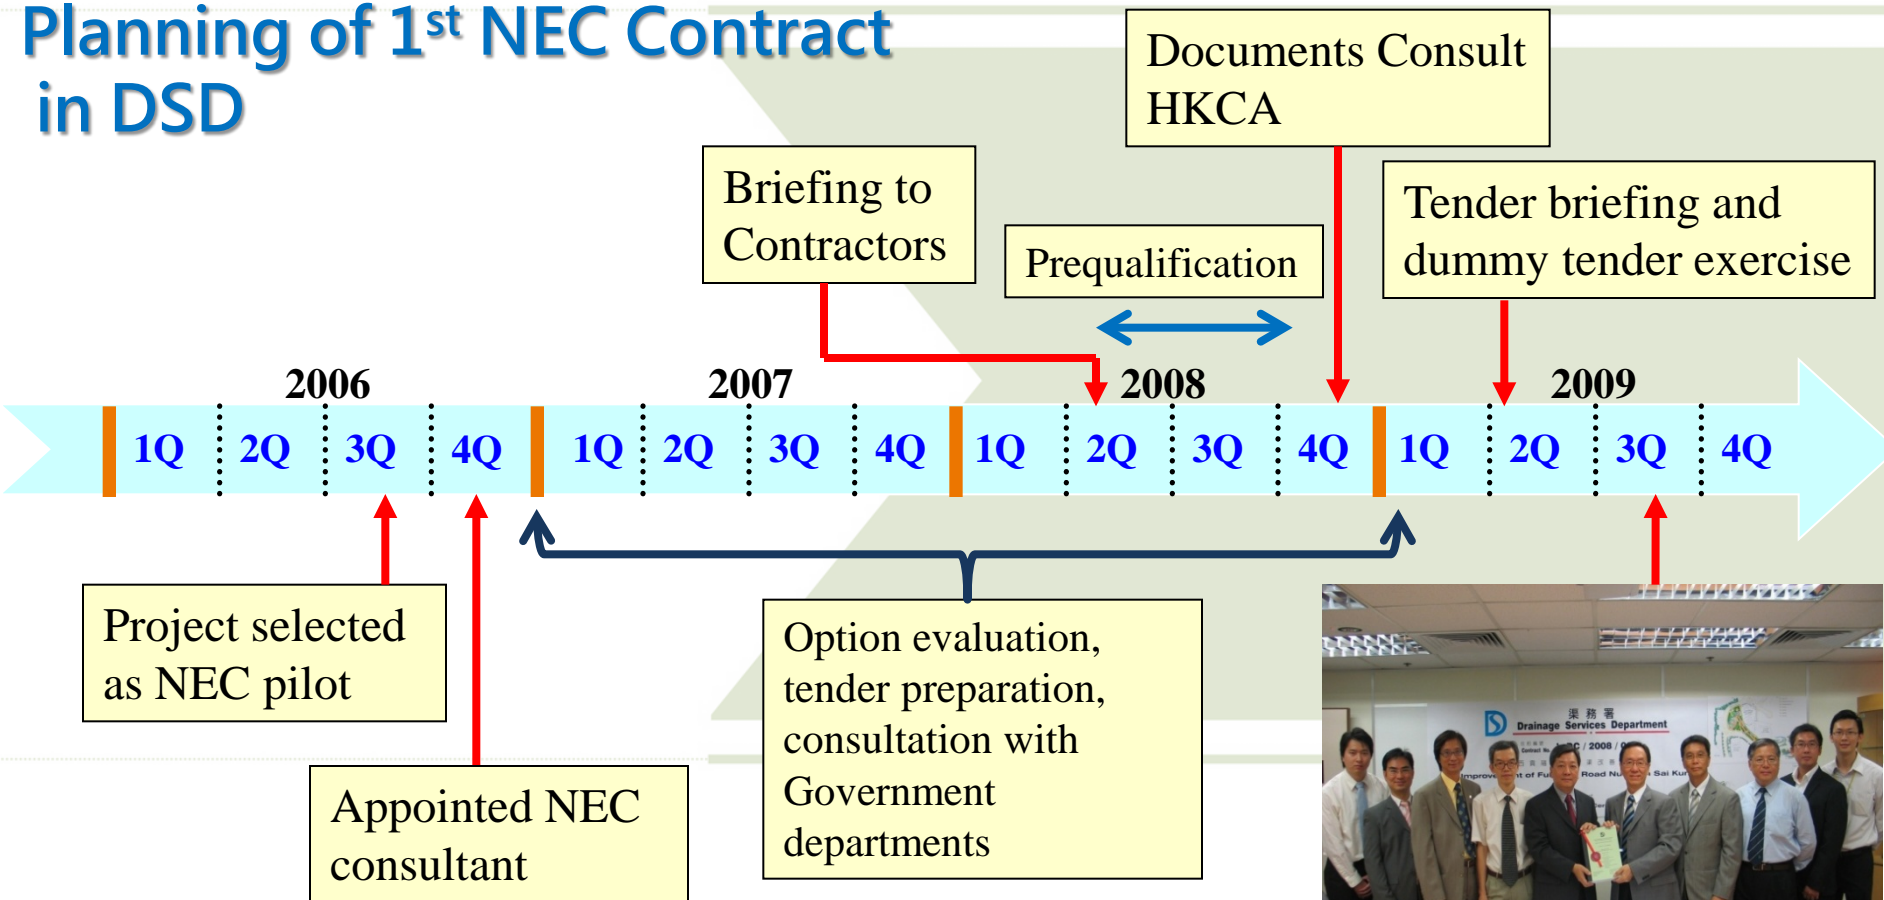

1st NEC Contract in DSD and in Hong Kong Government



- ***Improvement of Fuk Man Road Nullah in Sai Kung***
 - Decking 180m long 12m wide open nullah, road and landscaping works



Success in: Early completion by 6 months
Gain share of ~ 5%
Working relationship
Public Image

1st NEC Contract in DSD and in Hong Kong Government



Feedback from Public

- “DSD, Contractor and Consultant have put great effort in **enhancing communication** with local stakeholders and presenting progress of works to District Council members. ‘**More communication, fewer problems**’ - I do appreciate this new thinking approach”

Ng Sze-fuk, SBS, JP
Chairman

Sai Kung District Council



NEC Contracts in Hong Kong



DSD's current NEC Contracts

Contract / Agreement No.	Contract / Agreement Title	Contract Sum	Nature	Start / Completion	NEC Contract
DC/2008/02 <i>Consultant</i>	Improvement of Fuk Man Road Nullah in Sai Kung	\$76M	Nullah Decking	Aug 2009 / May 2012 (C)	ECC Option C
DC/2012/09 <i>Consultant</i>	Pak Hok Lam trunk sewer and Sha Tau Kok village sewerage	\$203M	Village sewerage	June 2012 / Aug 2016	Framework + ECC Option B
DC/2012/03 <i>In-house</i>	Happy Valley underground stormwater storage scheme	\$678M	Flood prevention	Sept 2012 / Apr 2018	ECC Option C
DC/2012/05 <i>Consultant</i>	Yuen Long and Kam Tin Sewerage	\$160M	Village sewerage	Sept 2012 / Sept 2016	ECC Option D
DC/2012/07 <i>Consultant</i>	Lam Tsuen village sewerage	\$173M	Village sewerage	Oct 2012 / Jan 2016	ECC Option B
DC/2012/01 <i>In-house</i>	Building and Civil Maintenance to DSD plant and facilities	\$160M	Maintenance	Dec 2012 / Nov 2016	TSC Option A
DE/2013/05 <i>In-house</i>	E&M Facilities for Sewage Pumping Stations	\$18.5M	E&M	Mar 2014 / Sep 2015	ECC Option C
CE 63/2013 <i>Consultant</i>	Drainage Improvement Works in Happy Valley	\$8.9M	IDC Consultancy	Apr 2014 / mid 2019	PSC Option G

DSD R&D Forum 2013 – NEC

(28-11-2013)



NEC Contracts in Hong Kong



Overall

- 17 ECC contracts by end 2013
- DEVB's policy:
 - Extend pilot on NEC form in 2015 and 2016

In the Pipeline

	ECC – Construction Contracts			PSC - Consultancy		
	2014	2015	2016	2014	2015	2016
DSD	7	27	13	1	2	4
All works departments in Hong Kong	13	48	43	5	4	6

Opportunities



■ *Risk Management*

- Risk register
- Early warning notice
- Risk reduction meetings



Extract from LegCo
Development Panel
Information Paper
CB(1)925/13-14(03)
dated 25.2.2014
- Challenges in Delivery
of the Capital Works
Programme

Risk Management by Contractual Partnering: NEC

30. For better risk management, Government has been using the New Engineering Contract (NEC) form, which emphasizes mutual trust and co-operation between the contracting parties, in some pilot public works contracts. The NEC form allocates contractual risk to the party best able to manage it. Moreover, it provides a collaborative risk management mechanism to reduce the chance of risk occurrence as well as mitigating the consequence when the risk is materialized. The sharing and management of risk in the NEC form could help reduce the cost to the project due to materialization of the risks.

Opportunities




■ *Early Risk Identification & Timely Joint Problem Solving*

Risk

- Conflict with HEC cables
- Progress hampered
- Impact on horse racing

Joint Problem Solving

- Joint advance planning
- Secured HKJC's agreement on TTA
- DSD's/HKJC's/HEC's contractors collaborated in cable diversion

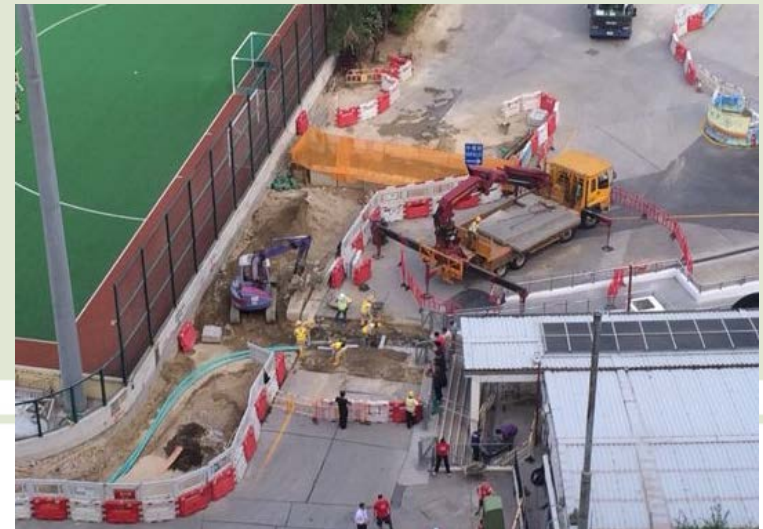

Diversion of HEC's Cable
by Joint Efforts

Opportunities



■ *Early Warnings and Risk Reduction*

Contract No.	No of Early Warning Notice Issued	No of Risk Reduction Meeting Held	No of Early Warning Notice Resolved
DC/2012/09	23	9	8
DC/2012/03	28	18	22
DC/2012/05	41	49	36
DC/2012/07	15	11	11
DC/2012/01	10	3	10


Opportunities



■ *Cost Control*

- Prospective compensation events
- Less dispute
- Early finalisation


Contract No.	No of CE notified	No of CE agreed
DC/2012/09	24	19
DC/2012/03	78	33
DC/2012/05	31	28
DC/2012/07	30	29
DC/2012/01	5	5



Opportunities



Cost Saving Design

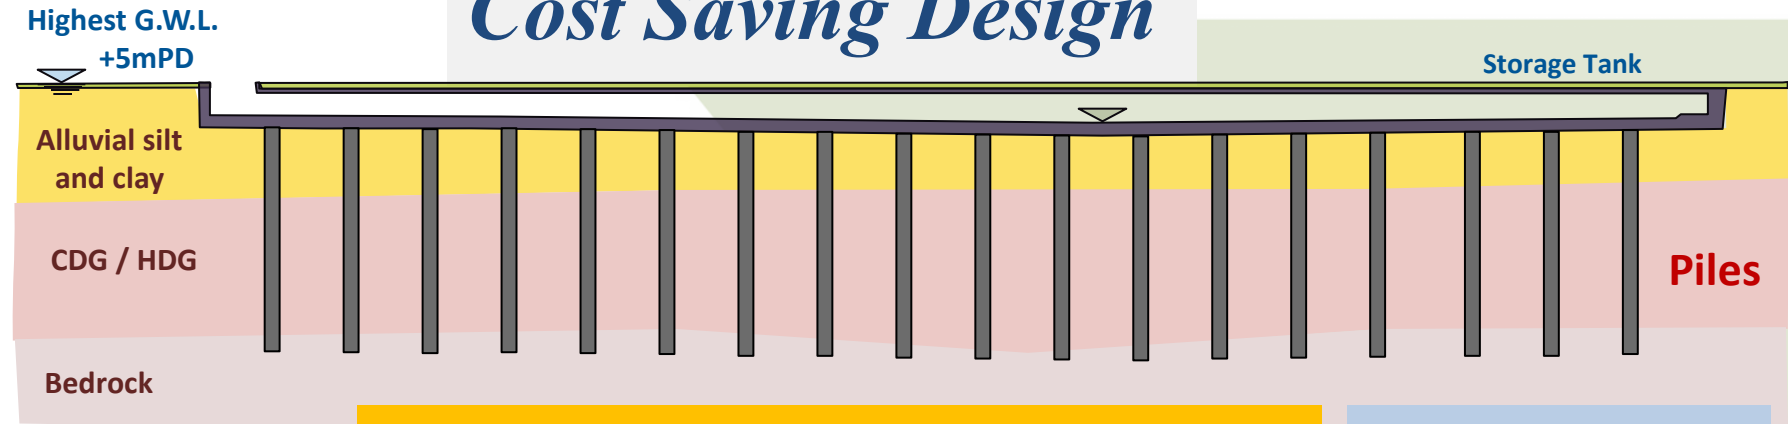


Early Approval

- Approval-in-principle: 2 months
- Final approval: 7 months
- Potential time saving: 5 months
- Potential cost saving: \$70M

Gain/pain share:

- Incentive to jointly drive final cost down

Original Design

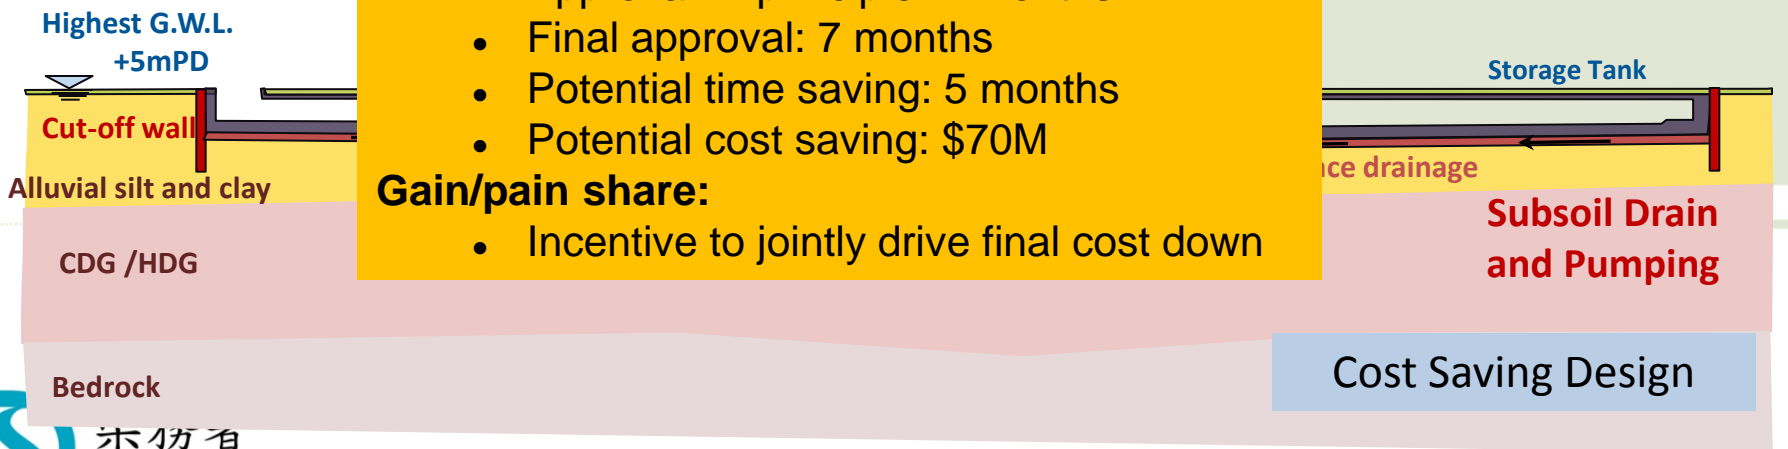

排水處

Drainage Services Department

Opportunities

■ *Staff Morale*

- Team spirit / harmony
- Stakeholders' satisfaction
- Achievement




DSD / Contractor

Site Housekeeping Award 2013



Mobile Messenger Device

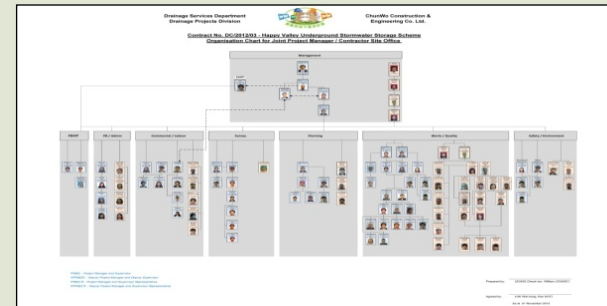

Joint Organization Chart



Stakeholders Workshop:
District Council members, HKJC, LCSD,
Contractor, Subcontractors




Opportunities



Partnering Scores

Down Trend
(due to increased difficulties on site)

Up Trend
(after some success cases)

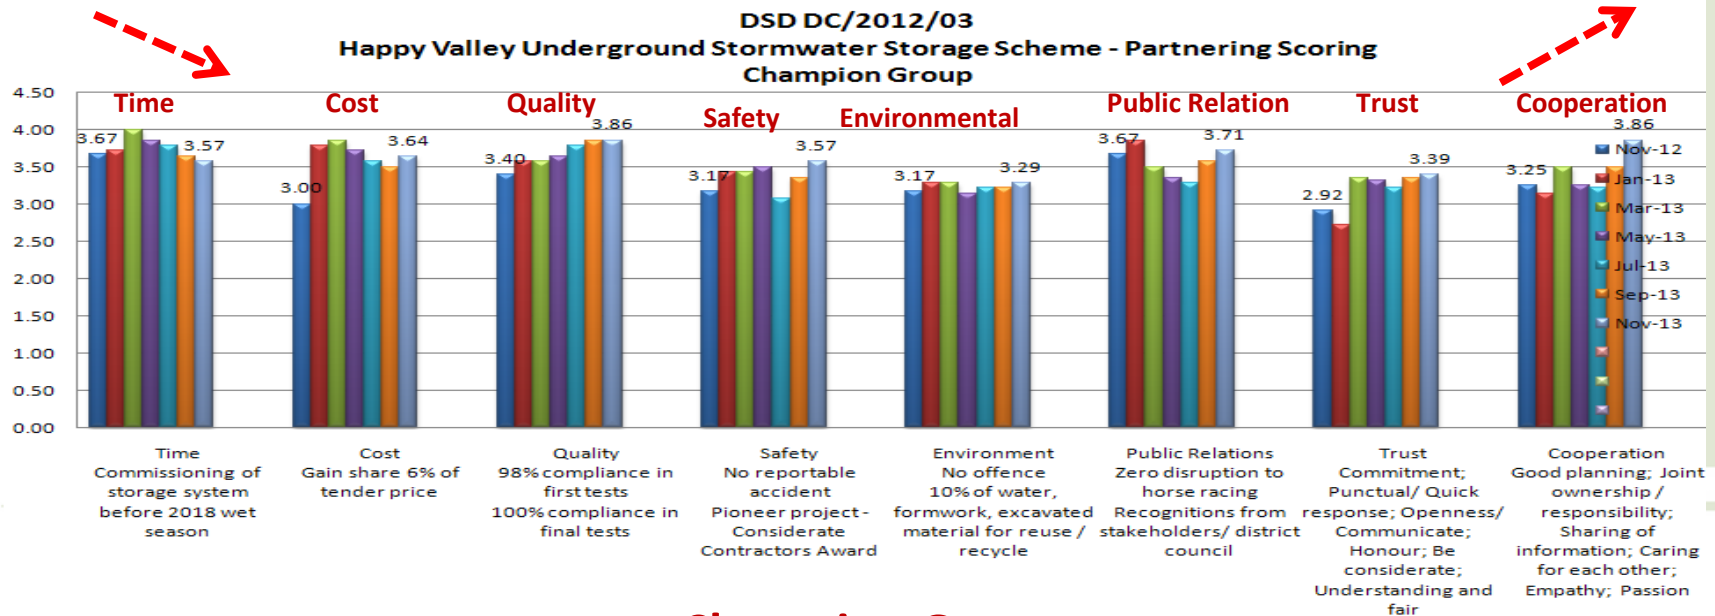

Champion Group

Challenges



■ *Lack of Knowledge / Experience*

- Form of contract
- Contractual terms
- Administrative procedure
- Programming
- Cost accounting



Challenges



■ *Resource Demanding*

- NEC advisory and project management
- Programming and costing
- Early intensive resources



渠務署

Drainage Services Department

Challenges



■ *Inherent Culture in All Levels*

- Status quo
- Risk averse
- Personal conviction/belief
- Greed
- Bureaucracy



Challenges



■ *Trade Practices*

- Preferred subcontractors
- Pre-bidding
- Open book accounting
- Tactical pricing
- Windfall profit



Challenges



■ *Scepticism*

- Purpose
- Accountability
- Liability
- Integrity
- Sustained effort



NEC Adaptation in Hong Kong



■ *Promote Partnering*



Joint Site Office



Birthday Party



Dragon Boat Racing Team



NEC Adaptation in Hong Kong



■ *Inclement Weather*

- Replace ECC Core Clause 60.1(13) by
 - (i) inclement weather and/or its consequences adversely affecting the progress of the *works*, or
 - (ii) the hoisting of tropical cyclone warning signal No. 8 or above, or
 - (iii) a Black Rainstorm Warning.

NEC Adaptation in Hong Kong



■ *Hierarchy Clauses*

- For any ambiguity or inconsistency between any provision or document
- Adopted in PSC contracts
- Consider to be adopted in future ECC contracts



NEC Adaptation in Hong Kong



- ***Independent Administration and Cost Audit***

- Audit NEC practices
- Cost audit

- ***Financial Control and Auditing***

- Two-tier Payment Auditing Mechanism



渠務署

Drainage Services Department

NEC Adaptation in Hong Kong



■ *Dispute Resolution*

- NEC standard Dispute Resolution Options W1 and W2 not adopted in Hong Kong
- Hong Kong government's dispute resolution provisions added as Z-clauses
 - Mediation
 - Adjudication
 - Arbitration



渠務署


Drainage Services Department

NEC Adaptation in Hong Kong



■ *Pain-gain Share Mechanism*

- Pain – cap at 110% for Employer
- Gain – no cap

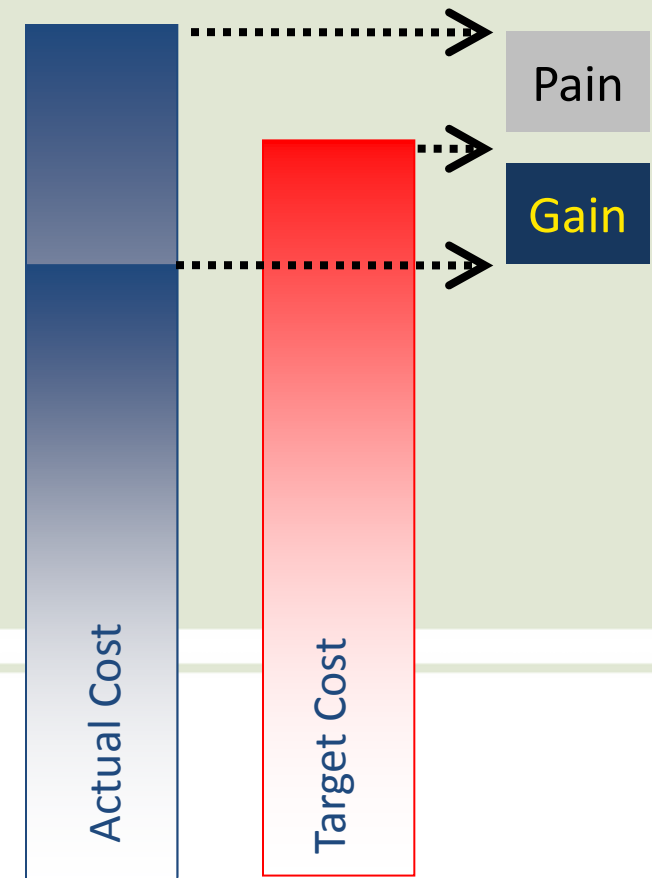

NEC Adaptation in Hong Kong



■ *Cash Positive to Cash Negative*

■ ECC Core Clause 11.2 (29)

“The Price for Work Done to Date is the total Defined Cost which the *Project Manager* ~~forecasts will have been paid by the Contractor before the next assessment date~~ plus the Fee.”

← assesses the *Contractor* has paid at each

■ Pay when paid



渠務署

Drainage Services Department



NEC Adaptation in Hong Kong



■ *Subcontracting*

- ACC Cl. C10 - Tender requirements for subcontracting
 - Different levels of procurement authority
 - More Project Manager's involvement
 - List of approved contractors / suppliers for sub-contracts >HK\$4.0M



渠務署


Drainage Services Department

NEC Adaptation in Hong Kong



■ *Further Pursuit for Full Benefit*

- Options E & F
- Incentive
- Cash positive payment
- Pain/gain share methodology
- Sub-contracting

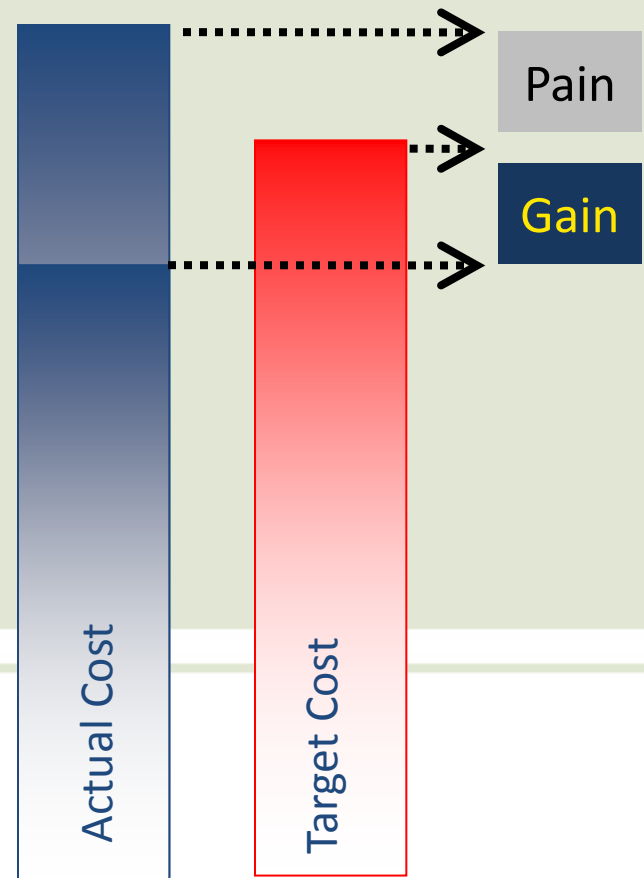

渠務署

Drainage Services Department

Thank You

DSD International Conference 2014

Sustainable Stormwater and Wastewater Management

12-14 November 2014
Hong Kong



Open for Registration:
15 March 2014

Deadline for Early Bird Registration:
15 August 2014

Hosted by:



渠務署
Drainage Services Department



follow us on



Conference Venue: Regal Hongkong Hotel
Enquiries: dsdic2014@icc.com.hk / +852 25599973

Website: www.dsdic2014.hk



Conference Sub-themes:



Stormwater Management

- A1 Green Strategies
- A2 Sustainable Urban Drainage System
- A3 Climate Change and Flood Risk Management
- A4 Asset Management
- A5 Hydraulics and Hydrology
- A6 Advances in Hydraulics and Water Quality Modelling



Wastewater Management

- B1 Nutrient Removal in Wastewater Treatment
- B2 Micro-pollutant in Wastewater Treatment and Disinfection
- B3 Odour Management
- B4 Compact Technology
- B5 Water Reuse
- B6 Energy Management

follow us on



Conference Venue: Regal Hongkong Hotel
Enquiries: dsdic2014@icc.com.hk / +852 25599973

Website: www.dsdic2014.hk

